




BAITA PLAI PROGRESS UPDATE MAY 2020



EXPECTED DEVELOPMENT SCHEDULE

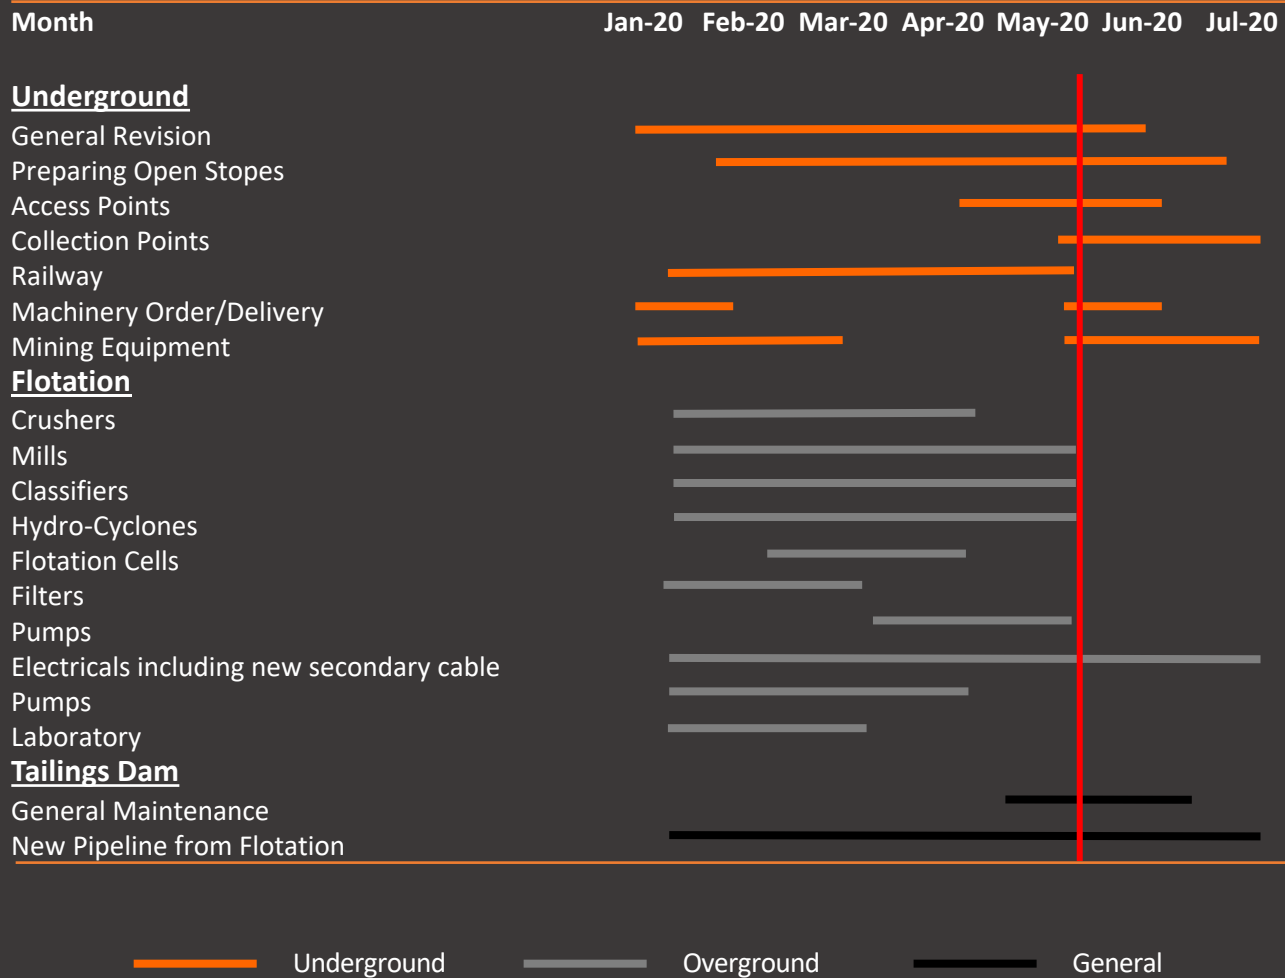

**In accordance to previously announced programme*

UPDATED DEVELOPMENT SCHEDULE

PROGRESS IS BEING MADE

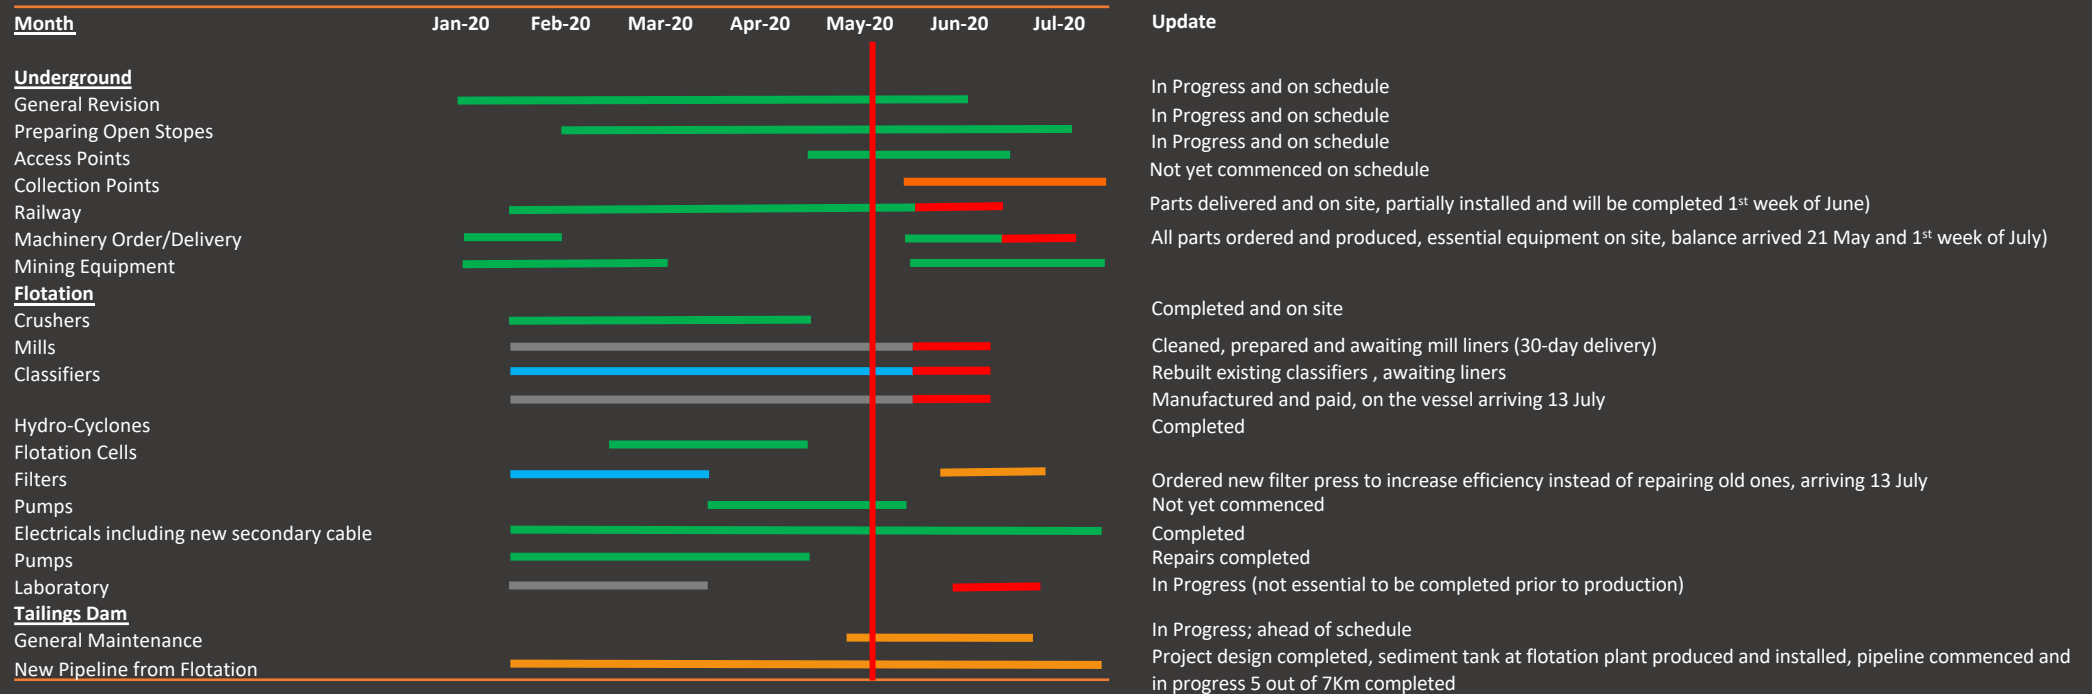

**In accordance to previously announced programme*

UPDATED DEVELOPMENT SCHEDULE

PROGRESS IS BEING MADE

Underground

1. General Revision



2. Preparing Open Stopes & 4. Collection Points



3. Access Points



UPDATED DEVELOPMENT SCHEDULE

PROGRESS IS BEING MADE

Underground

5. Railway



6. Machinery Order/Delivery & 7. Mining Equipment



Flotation

8. Crushers Mills



UPDATED DEVELOPMENT SCHEDULE

PROGRESS IS BEING MADE

Flotation

9. Classifiers



10. Hydro-Cyclones



11. Flotation Cells



UPDATED DEVELOPMENT SCHEDULE

PROGRESS IS BEING MADE

Flotation

- 12. Filters &
- 13. Pumps



- 14. Electricals including new secondary cable



- 15. Pumps and Reagent tanks



UPDATED DEVELOPMENT SCHEDULE

PROGRESS IS BEING MADE

Flotation

16. Laboratory



Tailings Dam

17. General Maintenance



Before and After



Before and After

18. New Pipeline from Flotation

